

## Scope of Work

Bulk excavation activities will continue throughout the site in May, with tieback drilling, stressing, and corner brace installation occurring concurrently on the west side. Additionally, the installation of the dewatering platform on the northwest side is anticipated during the third week of the month.

## What to Expect



- Drilling activity from tieback installation.
- Excavation activity.



- Truck traffic at Gate #2 (Yorkville)
- Potential traffic disruptions.



• General noise, vibrations, dust and debris.




• Closure of curb lane on Avenue Rd to accommodate a covered walkway.

(See Figure 4 on page 2).



(Figure 2): Bulk excavation activity, view of south side of site.



(Figure 3): Progress of platform installation on west side of site.

# **Project**

138 Yorkville Avenue **Mixed-Use Development** 

# **Project Stage**

**Bulk Excavation and Tieback Drilling** 

## **Projected Timeline** for Excavation Activities

January 2024 to May 2024

### **Work Hours**

Monday to Friday 7:00a.m to 7:00p.m

#### **Contact Us**

**Emergency Contact Line** (416) 849-1523

General Inquiries info@138 york villeup dates.ca


Website

www.138yorkvilleupdates.ca







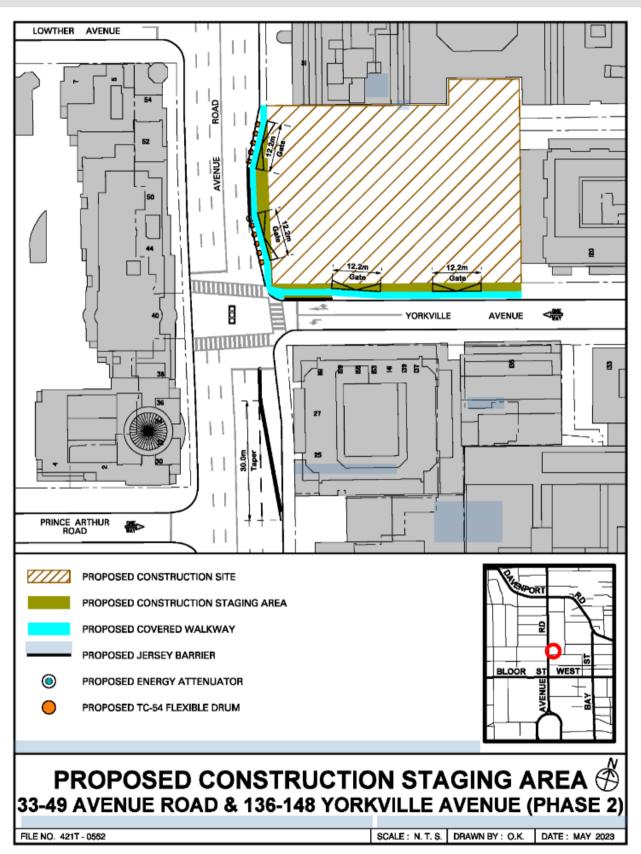

(Figure 4): Construction Staging Area - Updated March 2024
